


REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
WESTERN VISAYAS
PAROLA, ILOILO CITY



DETAILED ENGINEERING DESIGN PLANS
ESTABLISHMENT OF THREE(3) UNITS RAIN SHELTER
One(1) Unit at Antique, One(1) Unit at Capiz and One(1) Unit at Iloilo
(HVCDP 2025)

Prepared by:	Reviewed by:	Submitted by:	Recommending Approval:	Approved by:
 JERRY B. GUANCO, ABE Engineer II	 YVONNE GRACE H. SUR, ABE Head, FEAS	 MOISES D. MANAYAY, ABE, MEE Chief, FEED	 ENGR. JOSE ALBERT A. BARROGO RTO for Operation and Extension	 DENNIS R. ARPIA REGIONAL EXECUTIVE DIRECTOR

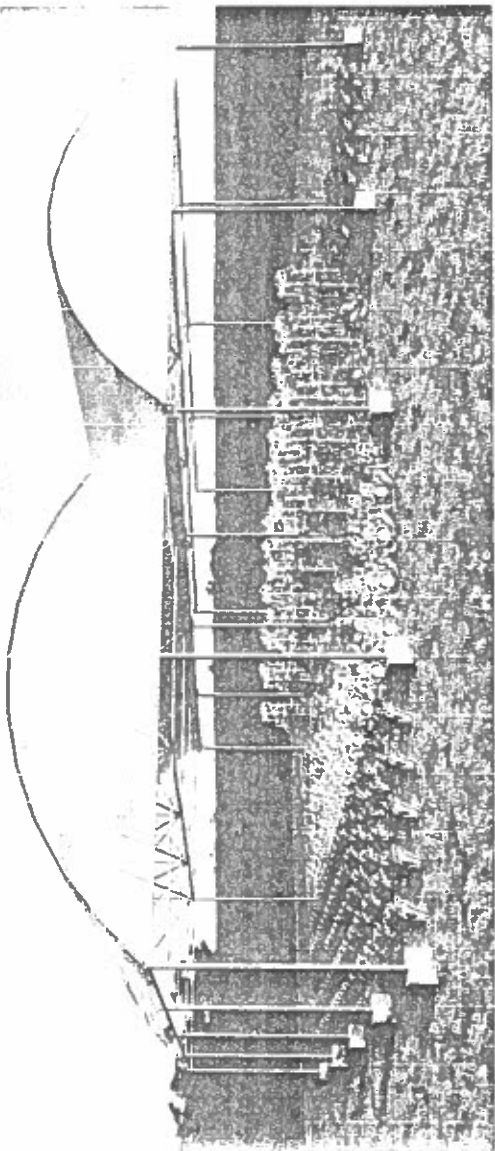

PERSPECTIVE VIEW

1 SCALE:
A-1

NTS


Item No.	Scope of Works	Qty	Unit
I OTHER GENERAL REQUIREMENTS			
B 9	MOBILIZATION/DEMOLITION	1 00	lot
B 5	PROJECT SIGNBOARD COA RUI BOARD	1 00	lot
B 7	OCCUPATIONAL SAFETY AND HEALTH	1 00	lot
II. EARTHWORKS			
800 0	CLEARING AND GRUBBING	84 56	sq m
803 0	STRUCTURAL EXCAVATION	1 10	cu m
1707 0	LEVELING COURSE	0 14	cu m
III. CONCRETE WORKS			
414 0	FORMWORKS	4 56	sq m
900 (1)	STRUCTURAL CONCRETE CLASS A	1 19	cu m
IV. ROOFING WORKS			
1013 0	ROOFING WORKS	96 00	sq m
V. STEEL WORKS			
1047 0	STEEL WORKS (GI PIPES AND CONNECTORS)	1 630 83	kg

2 SUMMARY OF QUANTITY

A-1 SCALE:

NTS

PHILIPPINE MAP

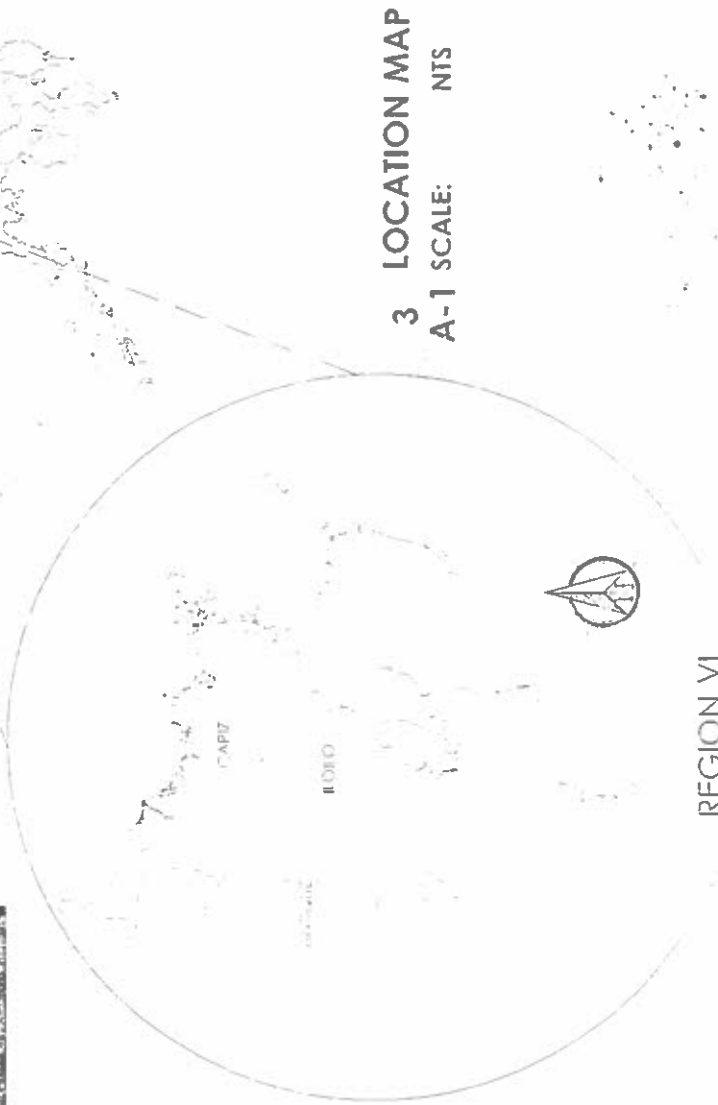

3 LOCATION MAP

A-1 SCALE: NTS



REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
WESTERN VISAYAS
BUREAU OF AGRICULTURE

UNITED STATES OF AMERICA
UNITED STATES OF AMERICA
UNITED STATES OF AMERICA

PERSPECTIVE VIEW
SUMMARY OF QUANTITIES
VEGETATION MAP


REVIEWED AND
APPROVED

APPROVED AND
APPROVED

APPROVED AND
APPROVED

APPROVED AND
APPROVED

APPROVED AND
APPROVED

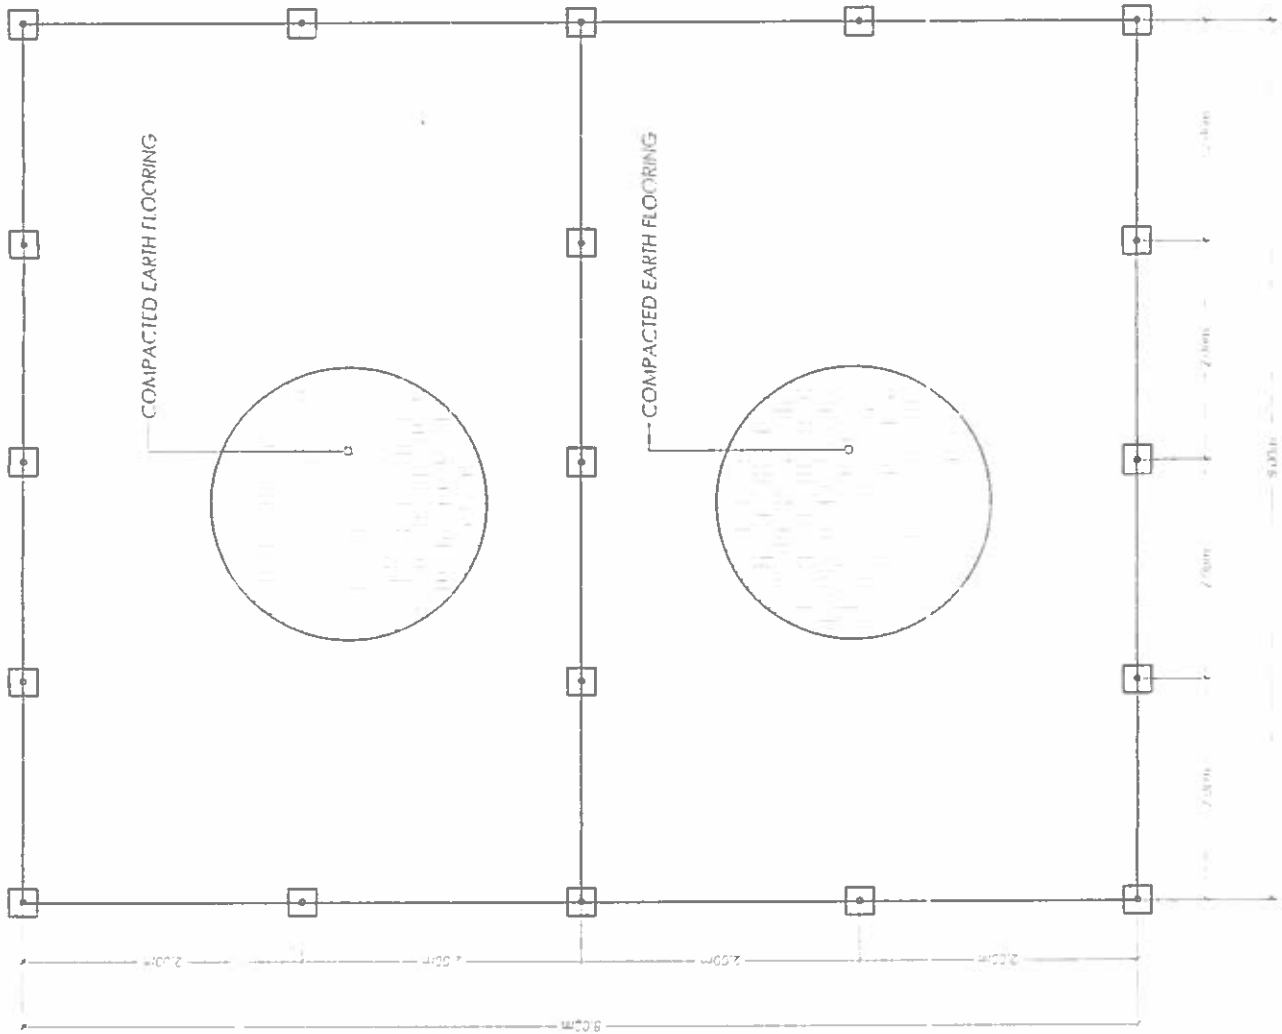

1 FLOOR PLAN
A-2 SCALE: NTS



REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
WESTERN VISAYAS
CAGAYAN DE ORO CITY

ESTABLISHMENT OF THREE (3)
GUIS RAFAEL SELLER
OFFICE: 1000-1000, 1000-1000

FOURTH


[Signature]
ARCHITECT

[Signature]
ARCHITECT

[Signature]
ARCHITECT


[Signature]
ARCHITECT

[Signature]
ARCHITECT

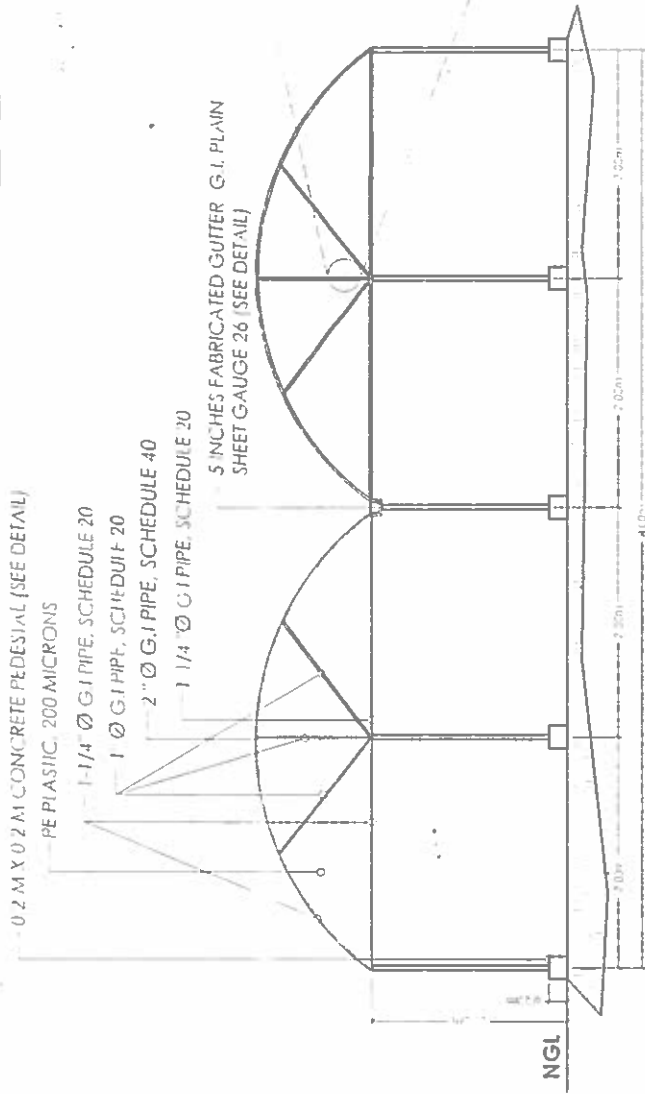


1 FRONT ELEVATION
A-3 SCALE: 1:60
NTS


NOTE:
PE PLASTIC MUST BE SECURED
USING C-CHANNEL PLATED
LAYERING AND ZIGZAG LOCK

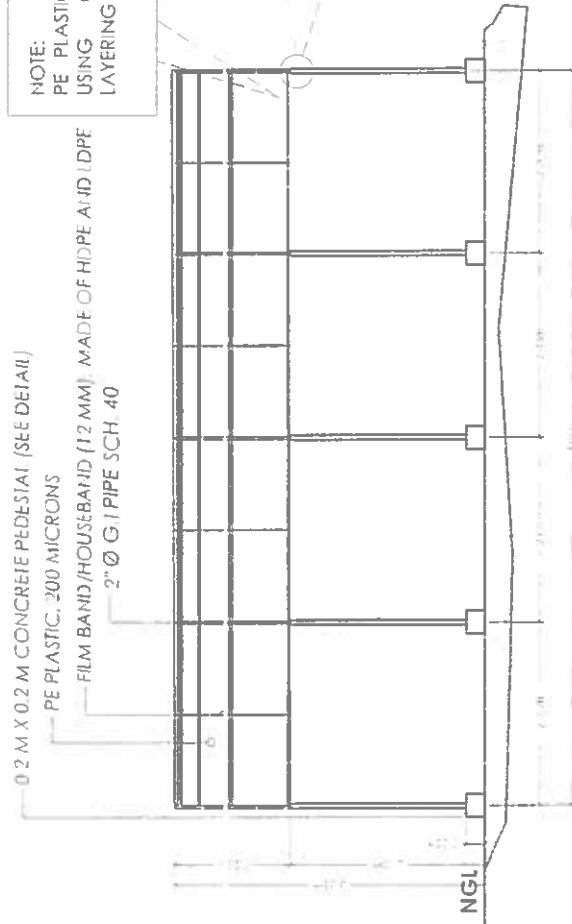

2 SIDE ELEVATION
A-3 SCALE: 1:60

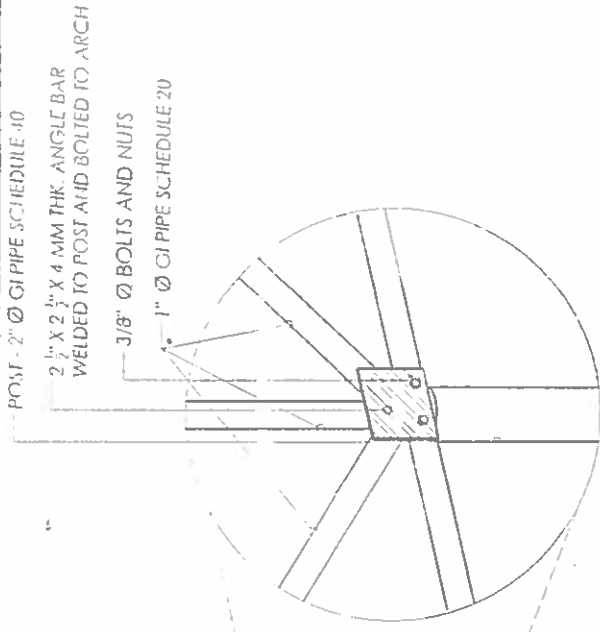

3 ARC CONNECTION DETAIL 1
A-3 SCALE: 1:5

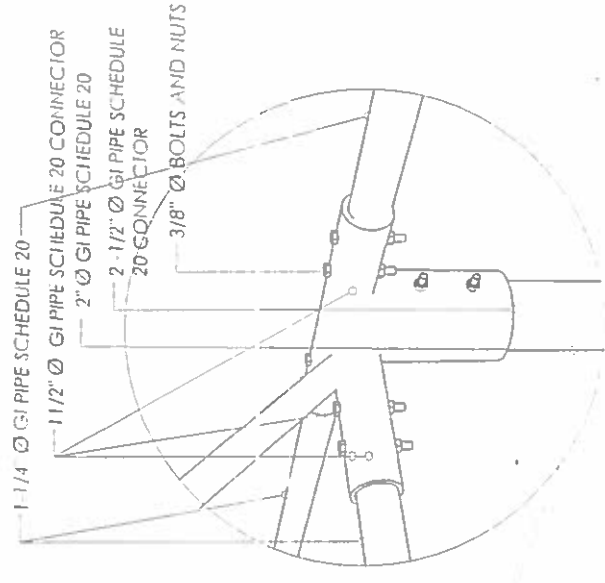

4 ARC CONNECTION DETAIL 2
A-3 SCALE: 1:5



REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
WESTERN VISAYAS
Davao Region

ESTABLISHED BY THE
UNITED STATES OF AMERICA
IN 1946

ARC CONNECTION DETAIL 1
ARC CONNECTION DETAIL 2

REVIEWED BY
JENNIFER GIANCOLONE
AT


DESIGNED BY
JENNIFER GIANCOLONE
AT

DESIGNED BY
JENNIFER GIANCOLONE
AT


DESIGNED BY
JENNIFER GIANCOLONE
AT

DESIGNED BY
JENNIFER GIANCOLONE
AT


DESIGNED BY
JENNIFER GIANCOLONE
AT

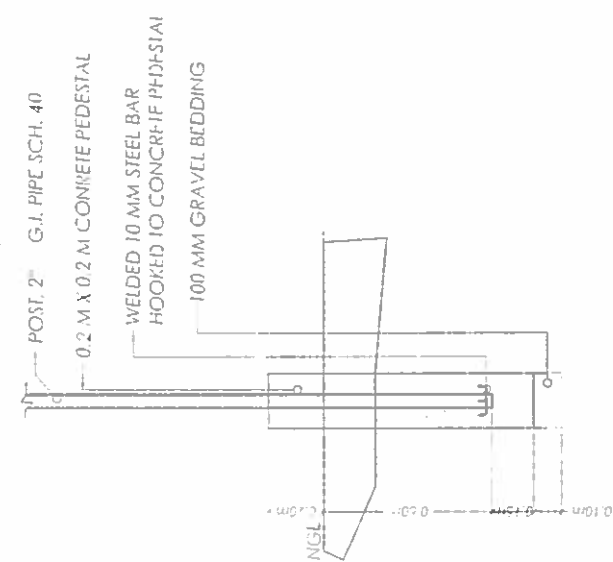


1 FOUNDATION DETAIL
A-4 SCALE: 1:20

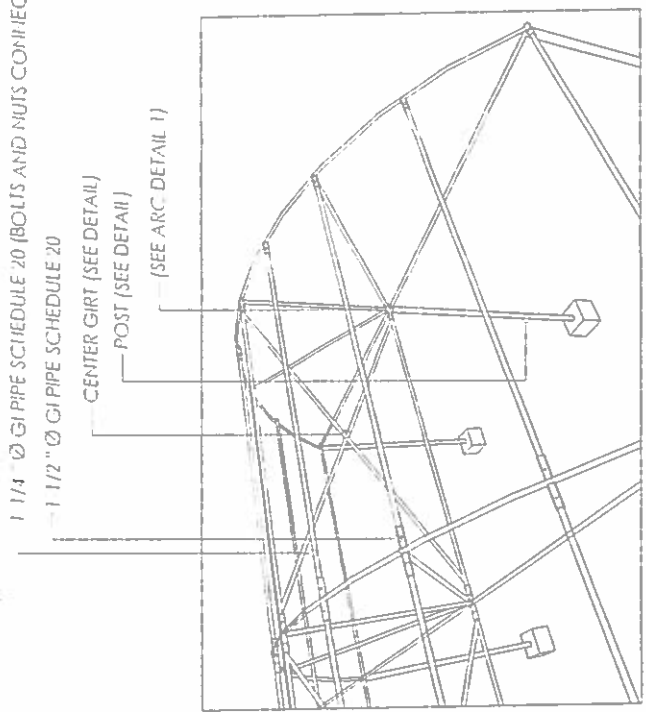


2 ARC CONNECTION DETAIL 3
A-4 SCALE: NTS

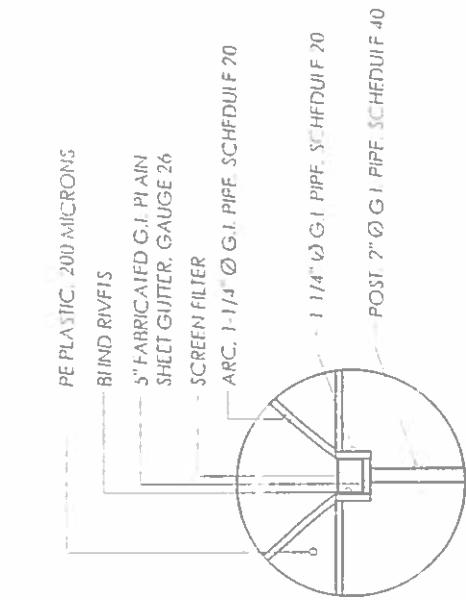

3 GUTTER DETAIL
A-4 SCALE: 1:20

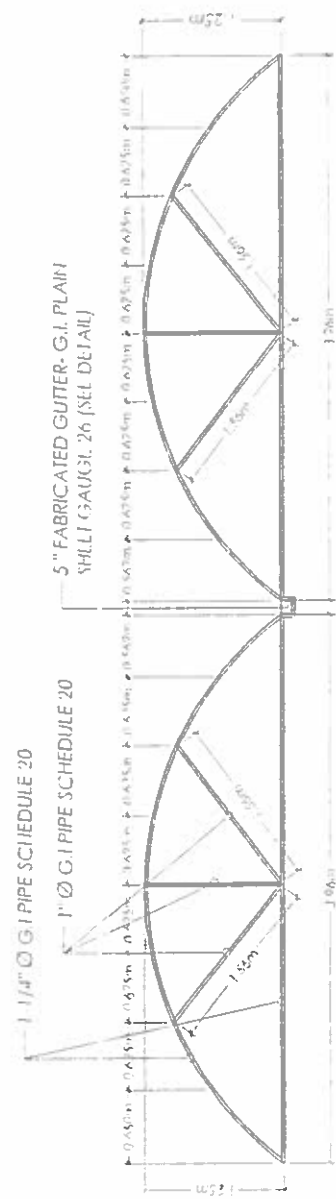


4 ARC FRAMING PLAN
A-4 SCALE: NTS

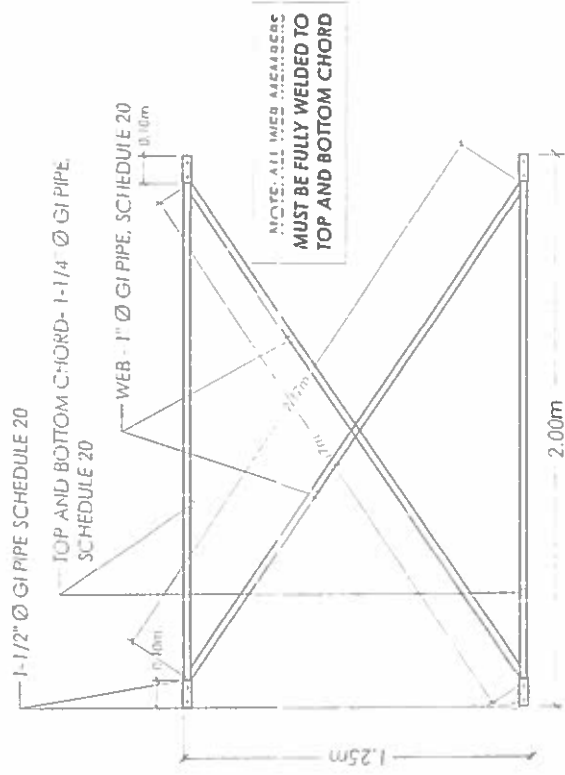

5 CENTER GIRT DETAIL
A-4 SCALE: 1:20

CONTRACTOR	NAME OF PROJECT
DATE STARTED	LOCATION
CONTRACT COMPLETION DATE	
CONTRACT COST	
IMPLEMENTING OFFICE	DEPARTMENT OF AGRICULTURE FIELD OFFICE VI
SOURCE OF FUND	


- THE BILLBOARD DESIGN LAYOUT AND DIMENSION SHALL BE ON A STANDARD BILLBOARD MEASURING 1200 mm x 2400 mm (4FT x 8FT.) USING 12 mm ($\frac{1}{2}$ INCH) THICK MARINE PLYWOOD OR TARPAULIN POSTED ON 5 mm ($\frac{3}{16}$ INCH) MARINE PLYWOOD.

PROJECT LOCATION		IMPLEMENTING AGENCY		DEVELOPMENT PARTNERS		CONTRACTOR SUPPLIER		BRIEF DESCRIPTION OF PROJECT		PROJECT DETAILS		FUND SOURCES	
DURATION	START/END	PROJECT DATE	TARGET DATE OF COMPLETION	PERCENTAGE OF COMPLETION	AS OF DATE	PROJECT STATUS	COST INCURRED TO DATE	DATE COMPLETED	REMARKS				
 <p>REPUBLIC OF SRI LANKA DEPARTMENT OF AGRICULTURE GOVERNMENT OF SRI LANKA</p>													
<p>FOR PARTICULARS OR COMMENTS ABOUT THIS PROJECT PLEASE CONTACT THE PROJECT MANAGER</p> <p>WHICH HAS AUDIT JURISDICTION ON THIS PROJECT</p>													
<p>CO-ORDINATING OFFICE NO. CLUSTER</p> <p>ADDRESS</p> <p>CONTACT NO.</p>													

TARPAULIN, WHITE, 8 FT x 8 FT
RESOLUTION: 70 DPI
FONT: HELVETICA
FONT SIZE: MAIN INFORMATION - 3"
SUB INFORMATION - 1"
FONT COLOR: BLACK

COA BILLBOARD
SCALE: NTS

[illegible]



Project Name:	ESTABLISHMENT OF THREE(3) UNITS RAIN SHELTER
Location:	One(1) Unit at Antique, One(1) Unit at Capiz and One(1) Unit at Iloilo
Project Duration:	63 CALENDAR DAYS
Total Estimated Project Cost:	Php. 900,000.00

START	PROJECT NO. 1	PROJECT NO. 2	PROJECT NO. 3	END
	78 CD	78 CD	78 CD	

NOTE PERT/CPM network diagram was adjusted/corrected for holidays, and sundays

Number of Working Days 63 days

Total Number of Calendar Days	63 days (PROJECT DURATION)
1	1
2	2
3	3
4	4
5	5
6	6
7	7
8	8
9	9
10	10
11	11
12	12
13	13
14	14
15	15
16	16
17	17
18	18
19	19
20	20
21	21
22	22
23	23
24	24
25	25
26	26
27	27
28	28
29	29
30	30
31	31
32	32
33	33
34	34
35	35
36	36
37	37
38	38
39	39
40	40
41	41
42	42
43	43
44	44
45	45
46	46
47	47
48	48
49	49
50	50
51	51
52	52
53	53
54	54
55	55
56	56
57	57
58	58
59	59
60	60
61	61
62	62
63	63

Prepared by:

Checked by:

JERRY B. GUANCO, ABE
Engineer II

YVONNE GRACE H. SUR, ABE
Head EPD's

~~MOISE D. MANA-AY, ADE, MEE~~
Division Chief, RA-10

ENGR. JOSE ALBERT A. BARROGO
RTD for Operation and Extension

DENNIS R. ARPIA
REGIONAL EXECUTIVE

Approved by:

Recommending Approval:

Year	1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047	2048	2049	2050	2051	2052	2053	2054	2055	2056	2057	2058	2059	2060	2061	2062	2063	2064	2065	2066	2067	2068	2069	2070	2071	2072	2073	2074	2075	2076	2077	2078	2079	2080	2081	2082	2083	2084	2085	2086	2087	2088	2089	2090	2091	2092	2093	2094	2095	2096	2097	2098	2099	2100
1997	1998	1999	2000	2001	2002	2003	2004	2005	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	2041	2042	2043	2044	2045	2046	2047	2048	2049	2050	2051	2052	2053	2054	2055	2056	2057	2058	2059	2060	2061	2062	2063	2064	2065	2066	2067	2068	2069	2070	2071	2072	2073	2074	2075	2076	2077	2078	2079	2080	2081	2082	2083	2084	2085	2086	2087	2088	2089	2090	2091	2092	2093	2094	2095	2096	2097	2098	2099	2100	

Appendix 1

	18 days	3 days	21 days
Number of Working Days	18	3	21
Sundays and Holidays	0	0	0
Total Number of Calendar Days	18	3	21


JERRY B. GUANCO, ABE
Engineer II


YVONNE GRACE, MSUR, ABE
Head, EPOSS

~~MOISEO. MANA-AY, AUE, MEE~~
Decision Chief: RAED

DEAN R. ARPIA
REGIONAL EXECUTIVE DIRECTOR

by
